



Lehi City Update

June 28, 2023


PROJECT OVERVIEW

LEHI CITY FIBER PROJECT


Notice to Proceed 17 May 2022	Demand Aggregation Launch 8 July 2022	Groundbreaking Ceremony 6 September 2022	Substantial Completion 17 May 2025
----------------------------------	--	---	---------------------------------------

LEHI CITY FIBER NETWORK

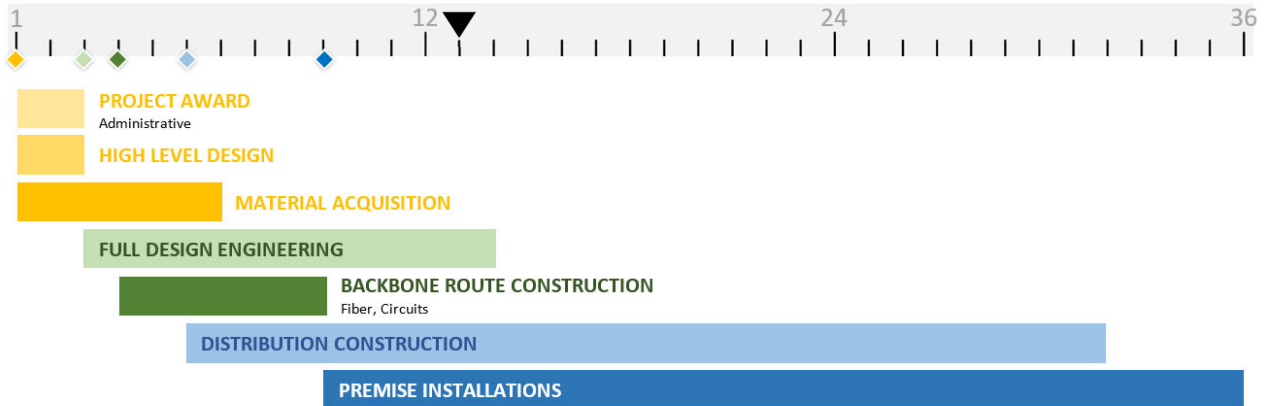



36-Month Project Timeline Summary

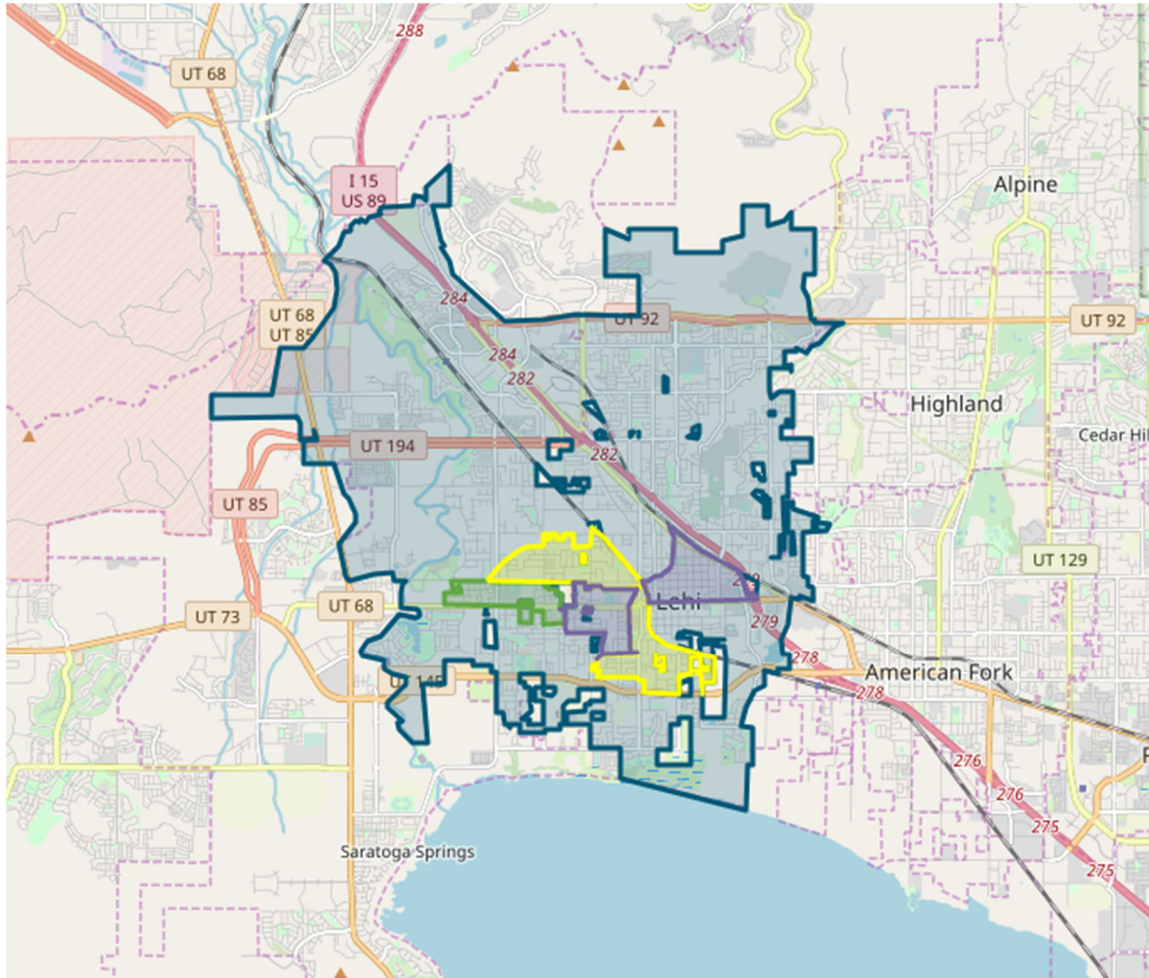

LEHI FIBER TO MY CITY MAP



LEGEND

	Lehi City
	Final Design and Planning
	Construction in Progress
	Fiber Ready – Contact ISP

ENGINEERING, CONSTRUCTION and NETWORK OPERATIONS

MID-LEVEL DESIGN

Mid-level designs identify fiber needs to city infrastructure within the project area, avoid negative impacts to existing Lehi Power aerial infrastructure, and identify sensitive areas where permitting and construction have the potential to affect the initial network backbone feeder route and beginning distribution areas.

- Field data collection for **cabinet areas 30, 38, and 40** are in progress.
- Field data collection is approximately **85% complete** for the entire project.

- The mid-level design reviews for **cabinet areas 2, 36, and 6** will take place in the next couple of weeks.

LOW-LEVEL DESIGN AND CONSTRUCTION DOCUMENTS

Construction drawings for cabinet areas will continue to be submitted on a once per week basis for city review.

- Upcoming cabinet area submittals include **cabinets 4, 3, and Backbone ring segment Shelter 4 to Shelter 3.**

Cabinet areas and projects will be scheduled to start construction after reviews are completed and permits are obtained.

- Currently approximately **38%** of all required network and cabinet areas have been reviewed and approved by the Lehi City review process.

SHELTER DESIGNS AND CONSTRUCTION

- Final installation and testing for the backup generators are being completed. Completion of the backup generators are the last remaining items to be completed for **shelters 1 and 2.**
- A secondary transport circuit has been installed into **shelter 1.** The second connection will provide additional protection for the fiber network and services to all customers.
- Construction for **shelter 4** is under way. The concrete foundation is anticipated to be installed in the next two weeks.

RING AND DISTRIBUTION FIBER CONSTRUCTION

- Construction has begun for the backbone ring section between **shelters 2 and 4.**
- Construction for **cabinet 18** will be completed in the next couple of weeks.
- Construction in **cabinet 9** is in progress.
- Cabinets **8 and 7** are anticipated to begin construction in the next couple of weeks.
- Once construction and fiber are completed in cabinets **18 and 9** all locations within the cabinet boundary may receive service for those citizens who choose to sign up. Notifications to the citizens informing them of service availability will occur as needed.
- Communication with citizens where cabinet areas will begin construction soon is in progress.
- Aerial make ready work by Lehi Power:
 - Complete in **cabinet areas 18, 9, 11, 7 and 8**
 - In progress in **cabinet areas 10 and 15**
 - Additional power make ready work in other cabinet areas will begin in the upcoming weeks.
- Joint use telecommunications make ready work in all cabinet areas is intended to be completed during the Lehi Fiber aerial installation.

CUSTOMER SERVICE INSTALLATIONS

Upon completing the signup process, each customer will meet with a Strata representative to schedule a fiber service drop at the customer's home, apartment, or business. Once completed, another Strata representative will meet with the customer to install the proper equipment for connectivity to the network.

Once a cabinet area is complete and ready for subscriber enrollment, residents in that area can sign up for service throughout the remainder of the project.

- For nearly one month, citizens within **cabinet area 5** have been able to sign up for service on the Lehi Fiber Network. Currently there are **72 residents** who have completed this process.
- Within the first month, approximately **15%** of available locations have subscribed for service on the Lehi Fiber Network.



The Peterson family poses with Lehi Mayor Mark Johnson on June 12th after their house was the first residence in the city to connect to the Lehi Fiber Network.

On June 12, 2023, we celebrated the successful connection of the first customer on the Lehi Fiber Network. The marketing team provided support for this event as well as worked to coordinate with V6 Media to capture the memorable day. V6 Media is working to produce a highlight film of the celebration that will be provided to Lehi soon.

As of June 19, 2023, the demand aggregation platform reached a total of 7,226 unique addresses registered within the city limits.

The marketing team has been actively assisting Lehi City with customer communication efforts by offering various assets and mailing lists. Additionally, during the Lehi Round-Up Celebration, our team coordinated with other Strata representatives to provide support at the Lehi Fiber Network booth. This was a great opportunity for our teams to participate in the Lehi community event and answer questions from residents.

Customer satisfaction surveys have been implemented. We will continue to monitor these surveys and provide monthly reports to Lehi City, keeping them informed about the results.
