




strata
NETWORKS



LEHI CITY FIBER NETWORK MONTHLY UPDATE

July 2023

LEHI FIBER TO MY CITY MAP

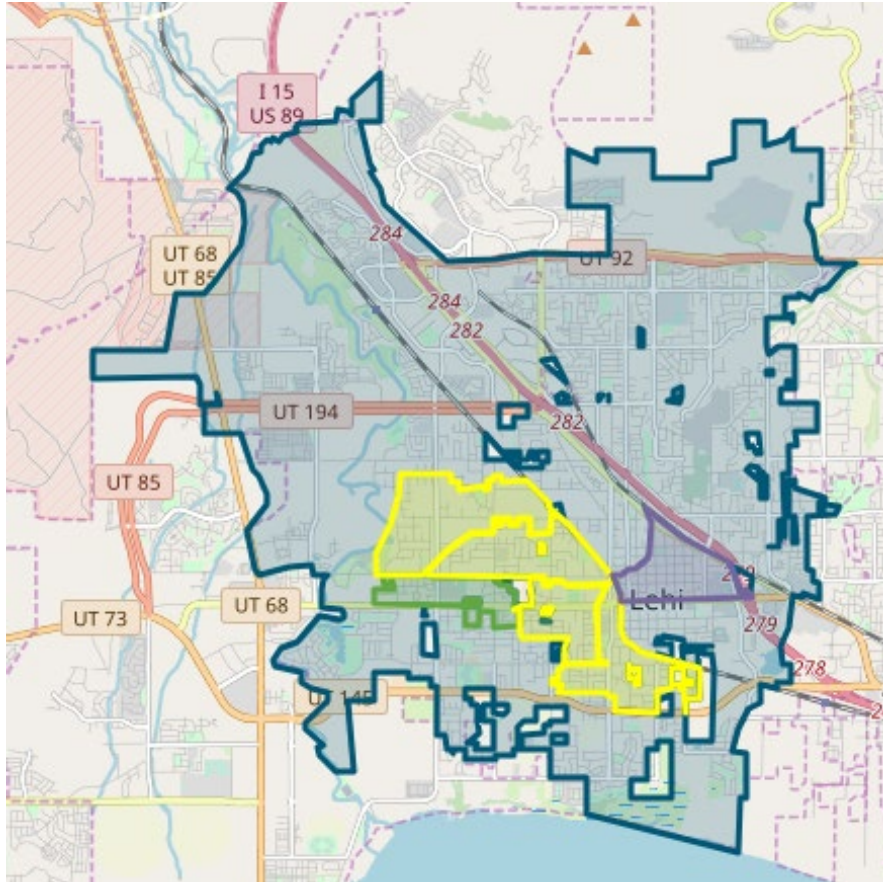

PROJECT OVERVIEW

NOTICE TO PROCEED

17 May 2022

DEMAND AGGREGATION LAUNCH

8 July 2022

GROUNDBREAKING CEREMONY

6 September 2022

SUBSTANTIAL COMPLETION

17 May 2025

COMPLETED BORING

Approx. 2,350 feet


COMPLETED MICROTRENCHING

Approx. 48,000 feet

COMPLETED FIBER PLACEMENT

Approx. 65,470 feet

36-MONTH PROJECT TIMELINE

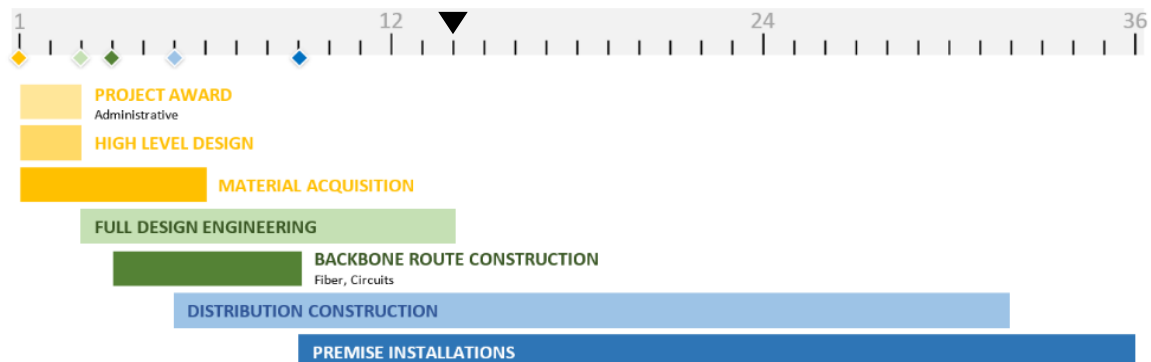

ENGINEERING, CONSTRUCTION and NETWORK OPERATIONS

MID-LEVEL DESIGN

Field data collection is approximately **99% complete** for the entire project.

Mid-level design reviews for **cabinet areas 33, 36, and backbone feeder route 3 to 1** will take place in the next couple of weeks.

LOW-LEVEL DESIGN AND CONSTRUCTION DOCUMENTS

Construction drawings for cabinet areas will continue to be submitted on a once per week basis for city review. Cabinet areas and projects will be scheduled to start construction after reviews are completed and permits are obtained.

- Upcoming cabinet area submittals include **cabinets 2, 3, and 13B**.
- Currently approximately **43%** of all required network and cabinet areas have been reviewed and approved by the Lehi City review process.

SHELTER DESIGNS AND CONSTRUCTION

- Construction for **shelter 4** is in progress. The site work has been completed and the concrete has been scheduled for placement. The shelter 4 building fabrication is near completion.

RING AND DISTRIBUTION FIBER CONSTRUCTION

- Construction for backbone ring section between **shelters 2 and 4** is in progress.
- Construction for **cabinets 9 and 18** is nearing completion. Once construction is complete and fiber is placed, all locations within these cabinet boundaries may receive service. Notifications to the citizens informing them of service availability will be given at that time.
- Cabinets **7 and 8** have begun construction.
- Communication with citizens is in progress where cabinet areas will soon begin construction.



VAULT PLACEMENT



LAYING MASTIC

Aerial make ready work by Lehi Power is complete in **cabinet areas 18, 9, 11, 7, 8, 15A, & 15B**, and is in progress in **cabinet area 10**. Additional power make ready work in other cabinet areas will begin in upcoming weeks.

Joint use telecommunications make ready work in all cabinet areas is intended to be completed during the Lehi Fiber aerial installation.

CUSTOMER INSTALLATIONS

Approximately **18%** of available locations in the Lehi Fiber

Network have subscribed for service within the first two months. There are currently **85** residents who have completed the sign up process in **cabinet area 5**.



SHELTER #4 CONCRETE SLAB AND FOUNDATION

MARKETING/PUBLIC RELATIONS

As of July 23, 2023, the demand aggregation platform reached a total of **7,473** unique addresses registered within city limits.

This month the marketing team built a take-rate report that will serve as a valuable tool throughout the project. It will be updated on a monthly basis and provided to the city. Through the end of June, the report shows 77 customers subscribed to the network in the first cabinet area.

Additionally, the marketing team will provide monthly reports on customer satisfaction regarding customer installation and initial service.

As mentioned in the last report, Strata's marketing team has collaborated with V6 Media on a recap video of the first customer connection. We are proud to share that the video has been released on both Lehi and Strata channels.

The marketing team is also working closely with Lehi City on various marketing assets, including ongoing cabinet area communication and future campaign ideas.
