



strata
NETWORKS




LEHI CITY FIBER NETWORK MONTHLY UPDATE

September 27, 2023



LEHI FIBER TO MY CITY MAP

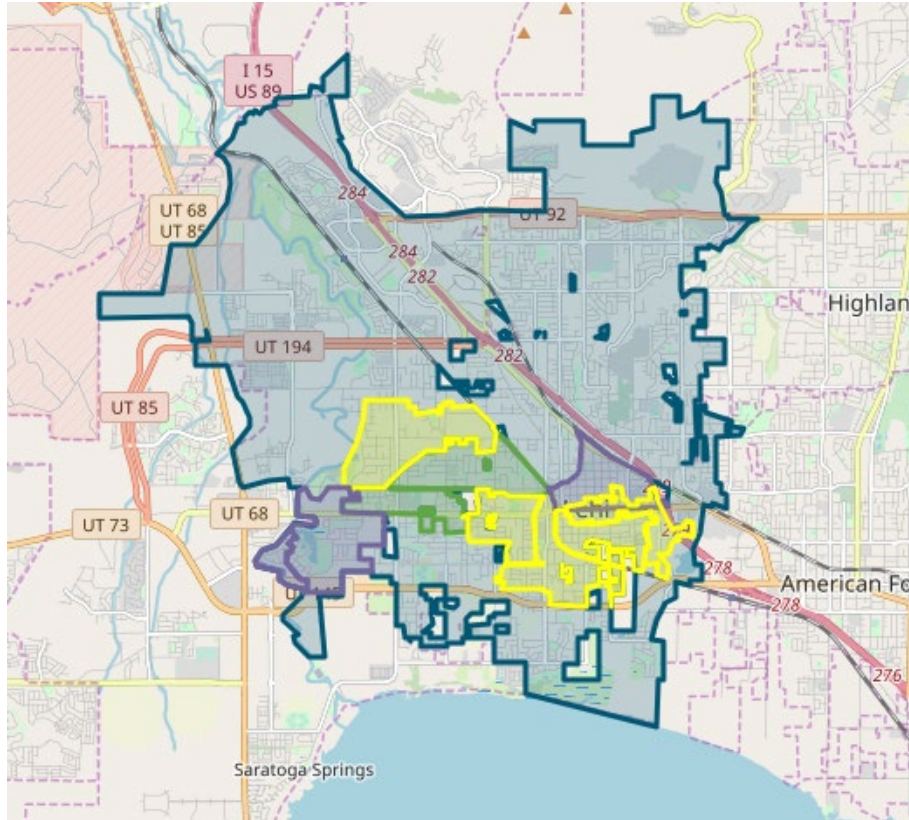

- Lehi City
- Final Design and Planning
- Construction in Progress
- Fiber Ready – Contact ISP

PROJECT OVERVIEW

NOTICE TO PROCEED

17 May 2022

DEMAND AGGREGATION LAUNCH

8 July 2022

GROUNDBREAKING CEREMONY

6 September 2022

SUBSTANTIAL COMPLETION

17 May 2025

COMPLETED BORING

Approx. 20,500 feet


COMPLETED MICROTRENCHING

Approx. 92,800 feet

COMPLETED FIBER PLACEMENT

Approx. 372,100 feet

36-MONTH PROJECT TIMELINE

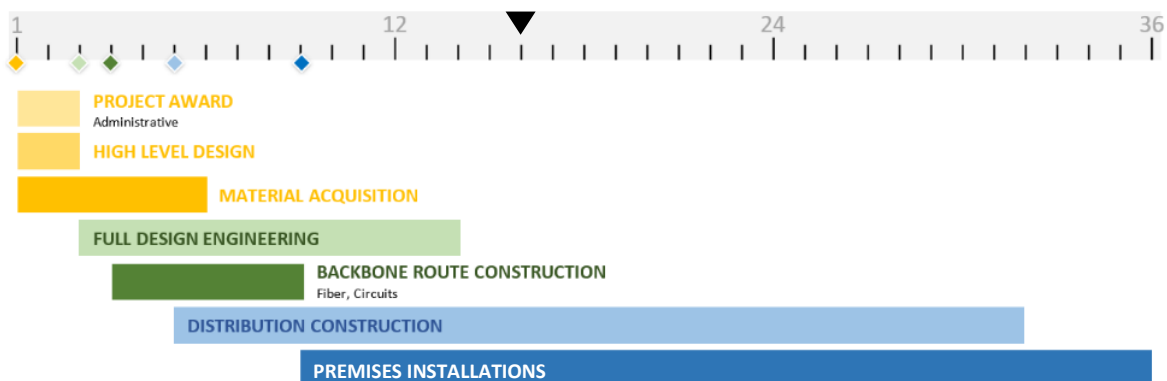



ENGINEERING, CONSTRUCTION and NETWORK OPERATIONS

MID-LEVEL DESIGN

Field data collection is 100% complete for the entire project.

Mid-level design reviews for the final six remaining network and cabinet areas will take place in the month of October.

LOW-LEVEL DESIGN AND CONSTRUCTION DOCUMENTS

Construction drawings for cabinet areas will continue to be submitted on a weekly basis for city review. Cabinet areas and projects will be scheduled to start construction after reviews are completed and permits are obtained.

- Upcoming cabinet area submittals include **cabinets 22, 34, 39, 29** and **37**.
- Currently approximately **60%** of all required network and cabinet areas have been reviewed and approved by the Lehi City review process.
- All remaining network and cabinet areas are anticipated to be submitted for city review in the next six weeks.

SHELTER DESIGNS AND CONSTRUCTION

- The site work and foundation construction for **shelter 3** is in progress. Once complete the building will be installed at the site.

RING AND DISTRIBUTION FIBER CONSTRUCTION

- Construction for backbone ring section between **shelters 1 and 3** will begin within the next two weeks.
- Fiber splicing for backbone ring section between **shelters 2 and 4** will be completed in the next couple of weeks. Once fiber splicing for this section is complete, **shelter 4** equipment can be turned up and activated on the network.
- Construction for **cabinets 8 and 9** are nearing completion. Once construction is complete and fiber is placed, all locations within these cabinet boundaries may receive service. Notifications to the citizens informing them of service availability will be given at that time.
- Fiber blowing and splicing for **cabinet 7** is under way. Customers located within this cabinet area will be able to sign up for service in the next two weeks.
- **Cabinets 10A and 10B** have begun construction.
- Construction for **cabinets 4A and 4B** will begin within the next two weeks.
- Communication with citizens is in progress where cabinet areas will soon begin construction.

Aerial make ready work by Lehi Power has been completed for the cabinets that are currently under construction. Additional power make ready work in other cabinet areas will begin in upcoming weeks.

Joint use telecommunications make ready work in all cabinet areas is intended to be completed during the Lehi Fiber aerial installation.

CUSTOMER INSTALLATIONS

Cabinet Area 5

- There are currently **97** residents who have completed the sign up process in cabinet area 5.



- Approximately **20%** of available locations in cabinet area 5 have subscribed for service.

Cabinet Area 18

- There are currently **139** residents who have completed the sign up process in cabinet area 18.
- Approximately **27%** of available locations in cabinet area 18 have subscribed for service.

MARKETING/PUBLIC RELATIONS

GREAT NEWS!

We are excited that construction has started in cabinet areas 10A and 10B! Working closely with Lehi City, we have reached out to residents in the area through mailers, emails, social media, and updates on lehi.fibertomycity.com.

DEMAND AGGREGATION

As of September 24, 2023, the demand aggregation platform reached a total of **7,757** unique addresses registered within city limits. The current network take rate is **23.04%**. This includes all customers who have signed up for service and are either active or pending.

FALL CAMPAIGN

This month the marketing team collaborated with the Lehi City team to create a fall campaign. The campaign encompasses various elements, including a targeted email campaign, a postcard, and several social media assets.
